


ID	Task Name	Start	Finish	Resource Names	2021 Qtr 3 Jul	Aug	Sep	2021 Qtr 4 Oct	Nov	Dec	2022 Qtr 1 Jan	Feb	Mar	2022 Qtr 2 Apr	May	Jun
0	Paulin, Tina PROJECT	Thu 21-08-12	Fri 22-03-18													
1	Project Initiation	Thu 21-08-12	Thu 21-08-12													
11	Order Windows & Ext Doors	Fri 21-08-27	Fri 21-08-27	Patsy												
12	Deliver Floor joists	Mon 21-08-30	Mon 21-08-30	SA Truss												
13	Framing 3 Floors	Tue 21-08-31	Wed 21-09-15	Dave Neufeld												
14	Roof Truss Delivery	Thu 21-09-16	Thu 21-09-16	SA Truss												
15	Framing roof system & Interior walls	Fri 21-09-17	Tue 21-09-28	Dave Neufeld												
16	Customer Framing Walkthrough	Wed 21-09-29	Wed 21-09-29	Neal & Tina Paulin												
17	Asphalt Shingle Delivery	Tue 21-09-28	Tue 21-09-28	Peter Weicker												
18	Install Asphalt Shingles	Wed 21-09-29	Tue 21-10-05	Peter Weicker												
19	Delivery Window & Exterior Door	Tue 21-10-19	Tue 21-10-19	Patsy												
20	Install Windows	Wed 21-10-20	Thu 21-10-21	Simon,Sam												
21	Install Exterior Doors	Fri 21-10-22	Fri 21-10-22	Joseph												
22	Notify bank - Lockup appraisal	Mon 21-10-04	Mon 21-10-04													
23	MILESTONE Lockup Bank Draw #1	Fri 21-10-22	Fri 21-10-22													
24	Plumbing roof vents	Wed 21-09-29	Wed 21-09-29	Justin Nash												
25	Plumbing Rough In Part 1	Thu 21-09-30	Wed 21-10-06	Justin Nash												
26	Plumbing Rough In Part 2	Thu 21-10-07	Mon 21-10-11	Justin Nash												
27	HVAC roof vent	Wed 21-09-29	Wed 21-09-29	Ryan Burt												
28	HVAC Rough In Part 1	Thu 21-10-07	Wed 21-10-13	Ryan Burt												
29	HVAC Rough In Part 2	Thu 21-10-14	Mon 21-10-18	Ryan Burt												
30	Request FORTIS BC Gas hookup	Tue 21-10-19	Tue 21-10-19	Patsy												
31	Backframing HVAC	Tue 21-10-19	Thu 21-10-21	Simon												
32	Install Fireplace	Fri 21-10-22	Fri 21-10-22	SA Fireplace												
33	Customer Electrical walk through	Tue 21-10-19	Tue 21-10-19	Neal & Tina Paulin												
34	Electrical Rough In Part 1	Wed 21-10-20	Tue 21-10-26	All Phase Electric												
35	Plumbing Fire suppression	Wed 21-10-27	Mon 21-11-01	Chapman Fire Protection												
36	Electrical Rough in Part 2	Wed 21-10-27	Fri 21-10-29	All Phase Electric												
37	Electrical Inspection	Mon 21-11-01	Tue 21-11-02	All Phase Electric												
38	Backframing Electrical	Mon 21-11-01	Tue 21-11-02	Simon												
39	Clean House Pre-Insulation	Wed 21-11-03	Wed 21-11-03	Simon												
40	Paper garage Floor	Thu 21-11-04	Thu 21-11-04	Simon												
41	Request Framing Inspection	Wed 21-10-27	Wed 21-10-27	Marc												
42	Framing Inspection	Mon 21-11-01	Mon 21-11-01	Sicamous,Dorvan												
43	Install Insulation	Wed 21-11-03	Mon 21-11-08	Dankoe Insulating												
44	Insulation Inspection	Tue 21-11-09	Tue 21-11-09	Dankoe Insulating												
45	Customer Pre-Drywall Walkthrough	Wed 21-11-10	Wed 21-11-10	Neal & Tina Paulin												
46	Driveway and Sidewalks	Thu 21-08-12	Thu 21-08-12	Dorvan												
47	Exterior Finish	Thu 21-09-30	Mon 22-03-07													
48	Prep for Decks and Railings	Tue 21-11-02	Wed 21-11-03	Dorvan												
49	Install Decking	Thu 21-11-04	Mon 21-11-08													
50	Install Exterior Railing	Thu 21-11-04	Mon 21-11-08													
51	Order Exterior Stone	Thu 21-09-30	Thu 21-09-30													



ID	Task Name	Start	Finish	Resource Names	2021 Qtr 3		2021 Qtr 4		2022 Qtr 1		2022 Qtr 2	
					Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
52	Exterior Stone	Wed 21-11-10	Thu 21-11-25	Jack Dullard								
53	Order Pine T & G Soffit	Fri 21-11-05	Fri 21-11-05									
54	Deliver Pine T&G to shop	Mon 21-11-08	Mon 21-11-08									
55	Paint Pine T & G	Tue 21-11-09	Fri 21-11-12									
56	Deliver Pine T & G Soffit to jobsite	Wed 21-11-24	Thu 21-11-25									
57	Order Siding Trim	Mon 21-11-08	Mon 21-11-08	Patsy								
58	Deliver Siding Trim to shop	Tue 21-11-09	Tue 21-11-09	Patsy								
59	Paint Siding Trim	Wed 21-11-10	Tue 21-11-16									
60	Deliver Siding & Soffit to jobsite	Wed 21-11-24	Thu 21-11-25									
61	Siding Installation	Fri 21-11-26	Thu 21-12-23	Joel Godbout								
62	Schedule Gutter installation	Mon 21-11-29	Mon 21-11-29	Marc								
63	Gutter and downspout installation	Fri 21-12-24	Fri 21-12-24	Cameron Exteriors								
64	Request Overhead doors	Tue 22-02-08	Tue 22-02-08	Patsy								
65	Install overhead doors garage	Mon 22-03-07	Mon 22-03-07	Vision Overhead doors								
66	Drywall boarding	Wed 21-11-10	Tue 21-11-23	Gord Jones								
67	Cut out Potlights	Wed 21-11-24	Wed 21-11-24	All Phase Electric								
68	Drywall Mud & tape	Wed 21-11-24	Tue 21-12-21	Gord Jones								
69	Notify bank appraisal draw #2	Tue 21-11-30	Tue 21-11-30	Patsy								
70	Milestone - Bank draw #2 - Drywall	Tue 21-12-21	Tue 21-12-21									
71	Tile - Bathroom showers	Wed 21-12-15	Tue 21-12-28	Jeremy Reimer								
72	Measure Shower Glass	Wed 21-12-29	Wed 21-12-29	Patsy								
73	Install Shower Glass	Wed 22-01-12	Wed 22-01-12	Patsy								
74	Fireplace Stone	Wed 21-12-29	Mon 22-01-03	Jeremy Reimer								
75	Paint Primer Coat	Wed 21-12-22	Thu 21-12-30	Steve Nunn								
76	Order Interior Doors & Trim	Tue 21-10-26	Tue 21-10-26	Patsy								
77	Deliver Interior Doors & Trim	Wed 21-12-15	Wed 21-12-15	Patsy								
78	Install Interior Doors & Trim	Fri 21-12-31	Fri 22-01-07	Joseph								
79	Paint colour Coat	Mon 22-01-10	Fri 22-01-14	Steve Nunn								
80	Install Cabinets and Vanities	Thu 22-02-10	Fri 22-02-18	Renaissance								
81	Measure countertops	Mon 22-02-21	Mon 22-02-21	Colonial								
82	Install Countertops	Tue 22-03-08	Tue 22-03-08	Colonial								
83	Install kitchen backsplash	Wed 22-03-09	Thu 22-03-10	Jeremy Reimer								
84	Deliver Ulay and Flooring	Mon 22-01-10	Mon 22-01-10	Patsy								
85	Install Ulay	Tue 22-01-11	Fri 22-01-14	Joseph								
86	Install Vinyl Plank Flooring	Mon 22-01-17	Wed 22-02-09	Rob								
87	Install Bathroom Infloor heat	Thu 22-02-10	Fri 22-02-11	Jeremy Reimer								
88	Install Bathroom floor tile	Mon 22-02-14	Mon 22-02-21	Jeremy Reimer								
89	Install hardwood flooring stairs	Tue 22-02-22	Fri 22-02-25									
90	Build Interior Railing	Mon 22-01-17	Fri 22-01-21	Joseph								
91	Install Interior Railing	Thu 22-02-10	Mon 22-02-14	Joseph								
92	Notify bank Draw #3 appraisal	Thu 22-02-17	Thu 22-02-17	Marc								
93	Milestone Bank draw #3 - Cabinets	Tue 22-03-08	Tue 22-03-08									
94	Delivery Baseboards & Trim	Thu 22-02-10	Thu 22-02-10	Patsy								

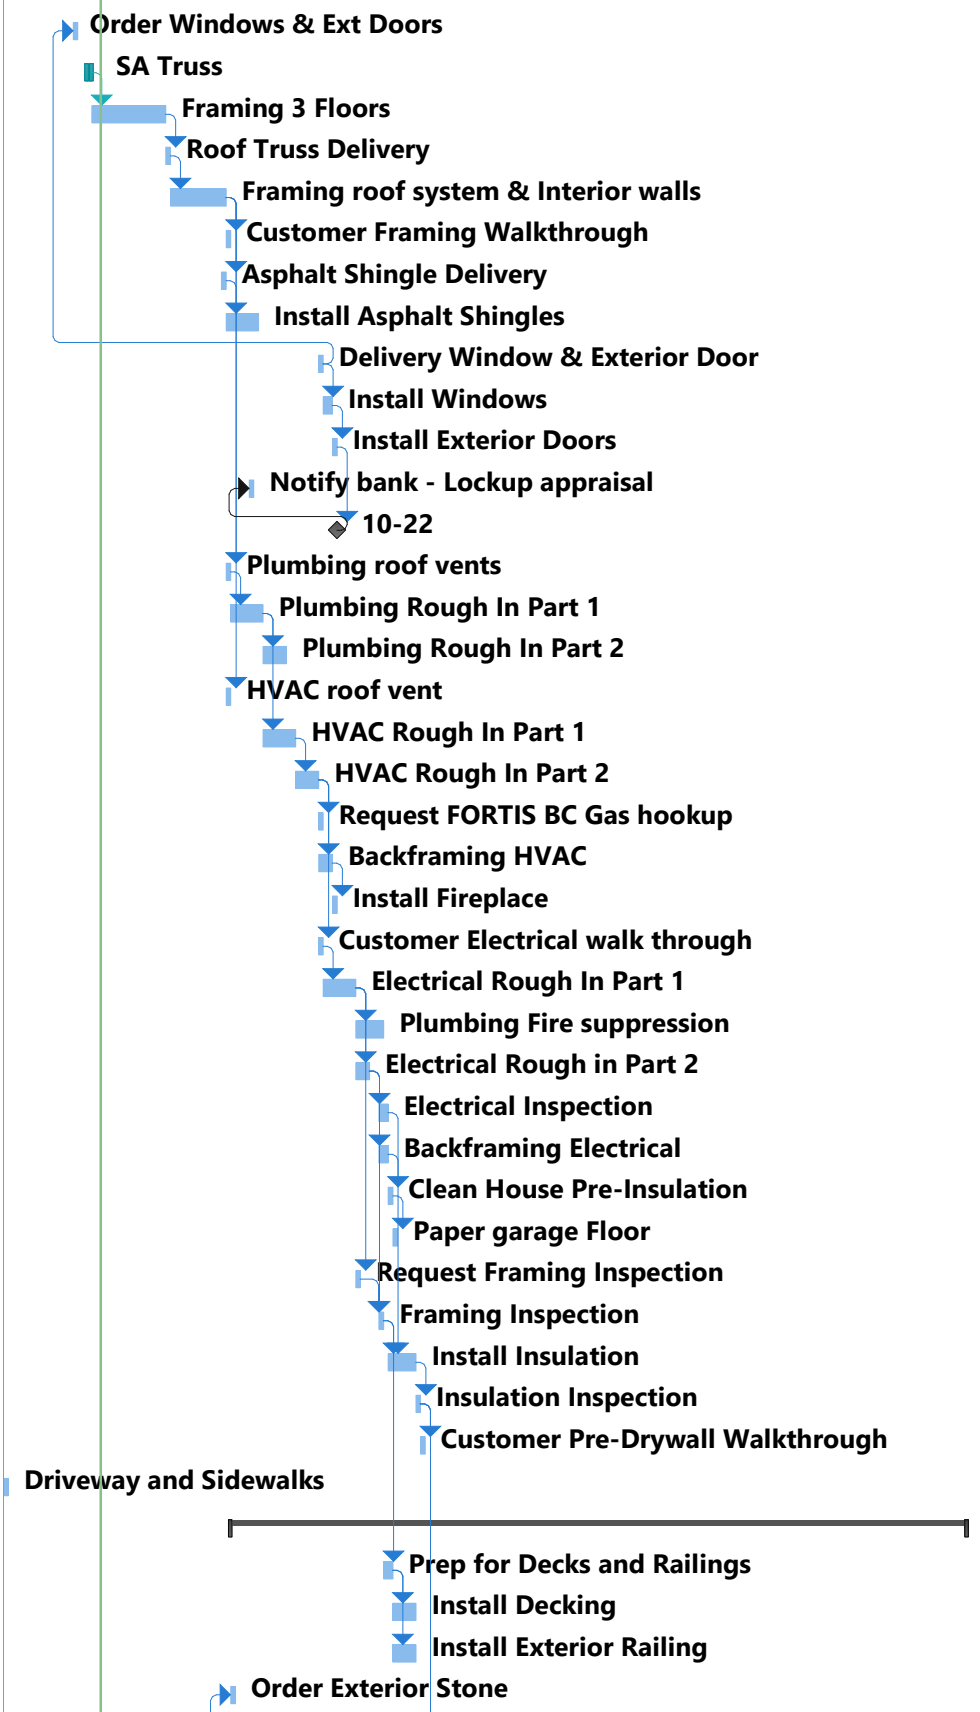
