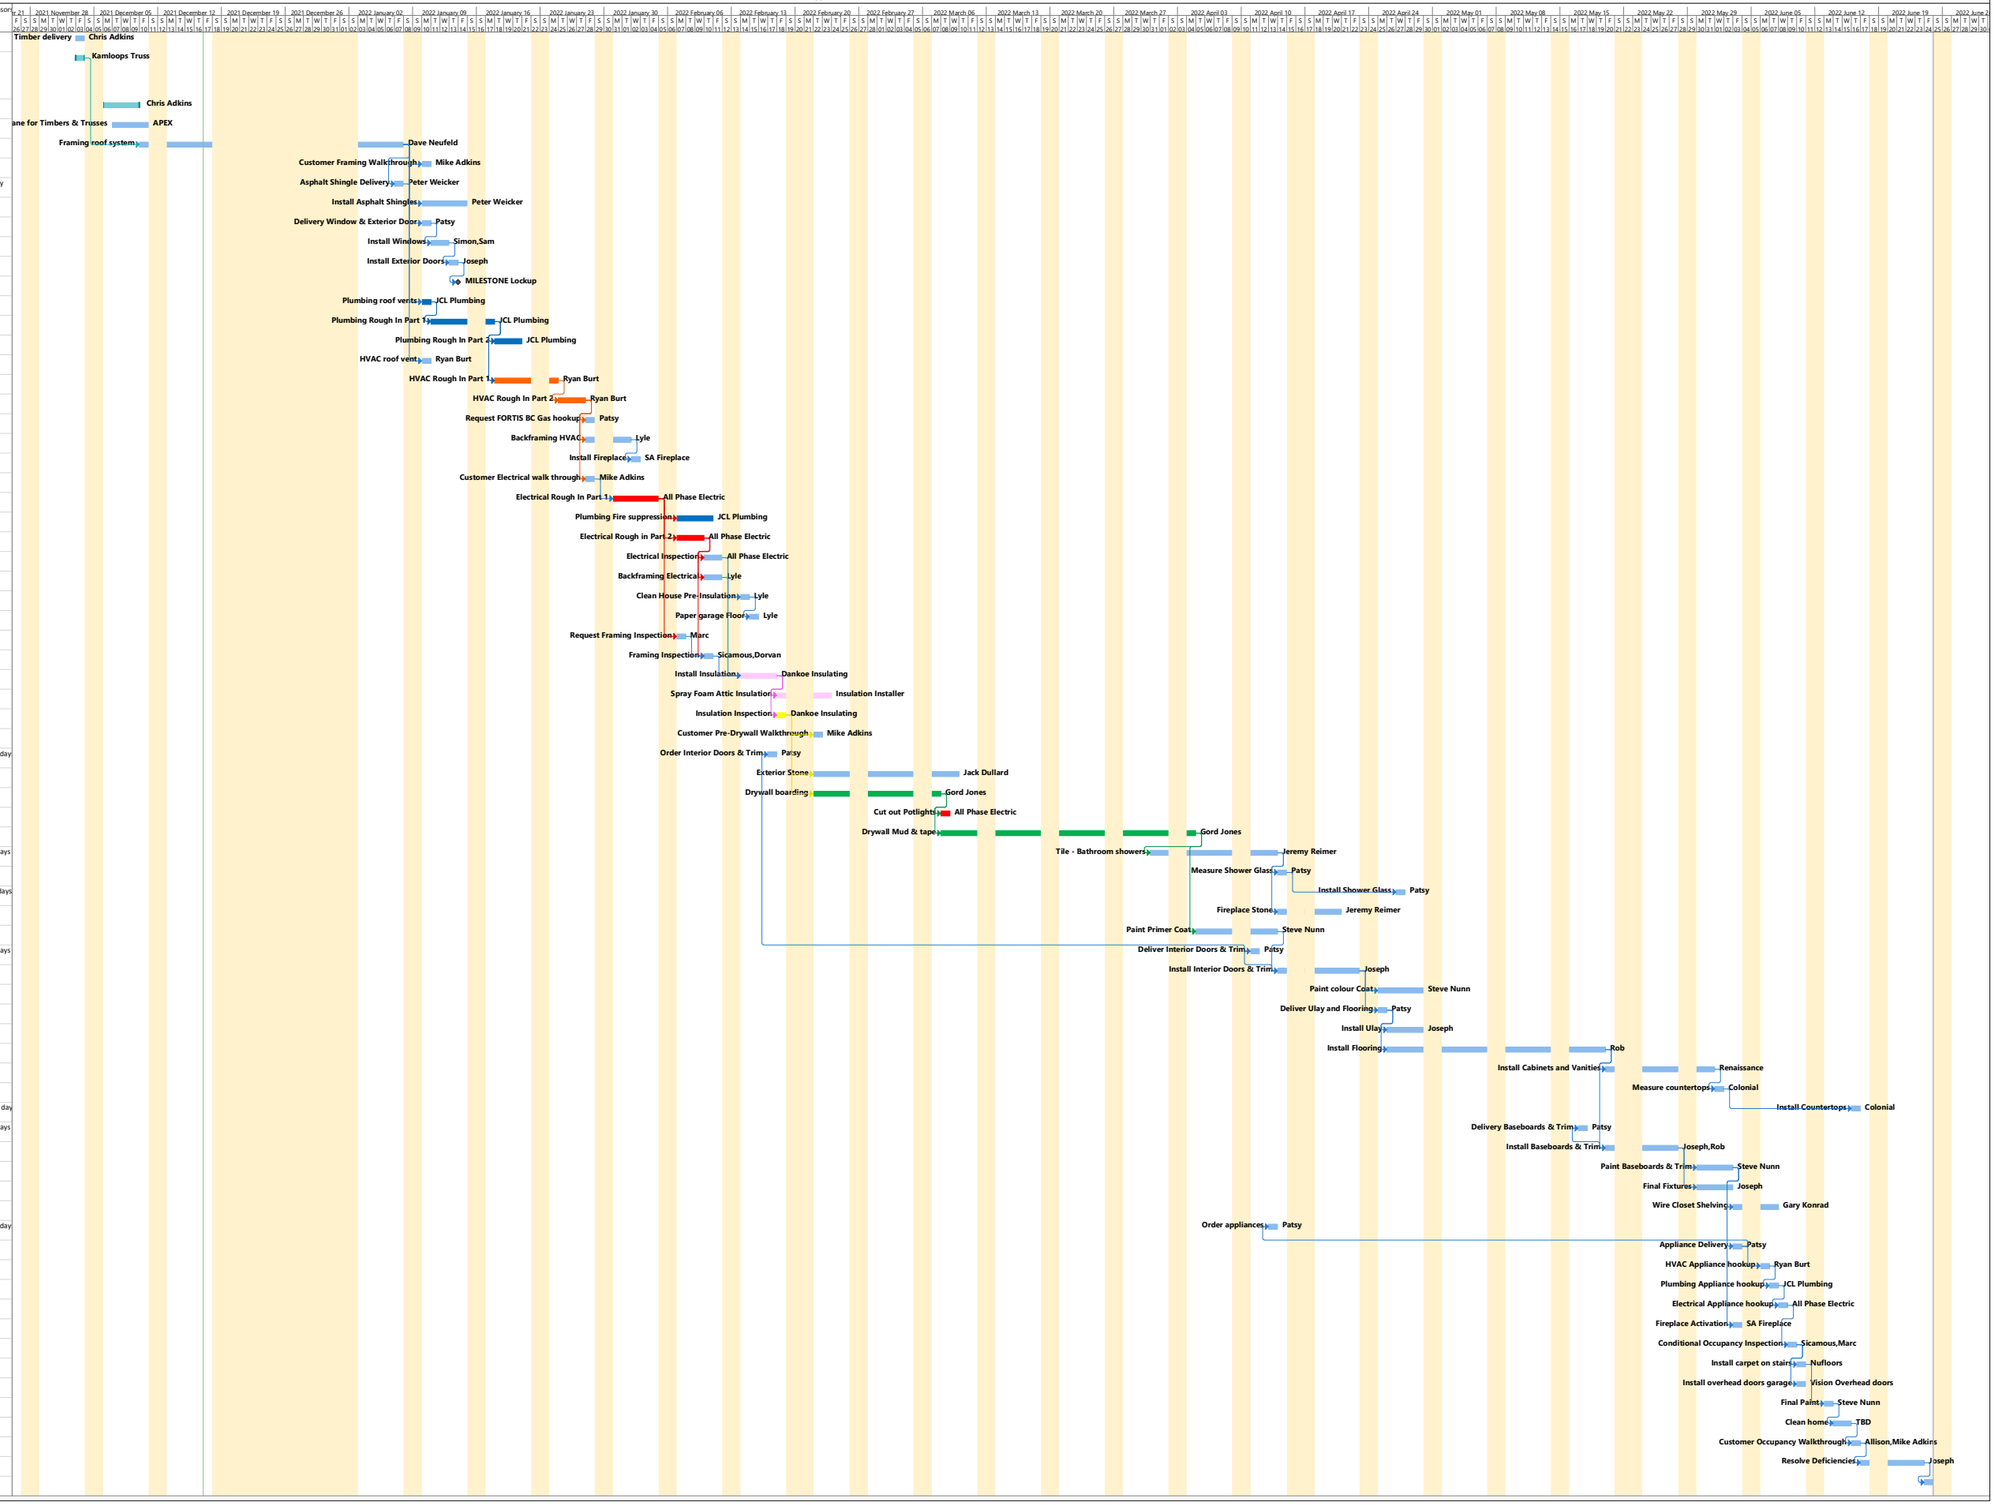ID	WBS	Task Name	Start	Finish	Resource Names	Duration	Predecessors
1	8.6	Timber delivery	2021-12-03	2021-12-03	Chris Adkins	1 day?	
2	8.2	Roof Truss Delivery	2021-12-03	2021-12-03	Kamloops Truss	1 day	
3	3	Timber Framing	2021-12-06	2021-12-09	Chris Adkins	4 days	
4	4	Crane for Timbers & Trusses	2021-12-07	2021-12-10	APEX	4 days	
5	8.6	Framing roof system	2021-12-10	2022-01-07	Dave Neufeld	11 days	2
6	8.0	Customer Framing Walkthrough	2022-01-10	2022-01-10	Mike Adkins	1 day	5
7	10.2	Asphalt Shingle Delivery	2022-01-07	2022-01-07	Peter Weicker	1 day	5FS-1 day
8	10.2	Install Asphalt Shingles	2022-01-10	2022-01-14	Peter Weicker	5 days	7
9	9.0	Delivery Window & Exterior Door	2022-01-10	2022-01-10	Patsy	1 day	5
10	9.10	Install Windows	2022-01-11	2022-01-12	Simon,Sam	2 days	9
11	9.10	Install Exterior Doors	2022-01-13	2022-01-13	Joseph	1 day	10
12	9.0	MILESTONE Lockup	2022-01-13	2022-01-13		0 days	11
13	12.0	Plumbing roof vents	2022-01-10	2022-01-10	JCL Plumbing	1 day	5
14	12.0	Plumbing Rough In Part 1	2022-01-11	2022-01-17	JCL Plumbing	5 days	13
15	12.0	Plumbing Rough In Part 2	2022-01-18	2022-01-20	JCL Plumbing	3 days	14
16	13.0	HVAC roof vent	2022-01-10	2022-01-10	Ryan Burt	1 day	5
17	13.0	HVAC Rough In Part 1	2022-01-18	2022-01-24	Ryan Burt	5 days	14
18	13.0	HVAC Rough In Part 2	2022-01-25	2022-01-27	Ryan Burt	3 days	17
19	13.0	Request FORTIS BC Gas hookup	2022-01-28	2022-01-28	Patsy	1 day?	18
20	8.7	Backframing HVAC	2022-01-28	2022-02-01	Lyle	3 days	18
21	13.0	Install Fireplace	2022-02-02	2022-02-02	SA Fireplace	1 day?	20
22	14.0	Customer Electrical walk through	2022-01-28	2022-01-28	Mike Adkins	1 day	18
23	14.0	Electrical Rough In Part 1	2022-01-31	2022-02-04	All Phase Electric	5 days	22
24	24.0	Plumbing Fire suppression	2022-02-07	2022-02-10	JCL Plumbing	4 days	23
25	14.0	Electrical Rough in Part 2	2022-02-07	2022-02-09	All Phase Electric	3 days	23
26	14.0	Electrical Inspection	2022-02-10	2022-02-11	All Phase Electric	2 days	25
27	8.7	Backframing Electrical	2022-02-10	2022-02-11	Lyle	2 days	25
28	8.7	Clean House Pre-Insulation	2022-02-14	2022-02-14	Lyle	1 day?	27
29	8.7	Paper garage Floor	2022-02-15	2022-02-15	Lyle	1 day?	28
30	8.7	Request Framing Inspection	2022-02-07	2022-02-07	Marc	1 day	23
31	8.7	Framing Inspection	2022-02-10	2022-02-10	Sicamous,Dorvan	1 day	25,30
32	15.0	Install Insulation	2022-02-14	2022-02-17	Dankoe Insulating	4 days	26,31
33	33	Spray Foam Attic Insulation	2022-02-18	2022-02-23	Insulation Installer	3 days	32
34	15.0	Insulation Inspection	2022-02-18	2022-02-18	Dankoe Insulating	1 day	32
35	15.0	Customer Pre-Drywall Walkthrough	2022-02-22	2022-02-22	Mike Adkins	1 day?	34
36	17.1	Order Interior Doors & Trim	2022-02-17	2022-02-17	Patsy	1 day?	46SS-36 day
37	10.1	Exterior Stone	2022-02-22	2022-03-09	Jack Dullard	12 days	34
38	16.0	Drywall boarding	2022-02-22	2022-03-07	Gord Jones	10 days	34
39	14.0	Cut out Potlights	2022-03-08	2022-03-08	All Phase Electric	1 day	38
40	16.0	Drywall Mud & tape	2022-03-08	2022-04-04	Gord Jones	20 days	38
41	18.0	Tile - Bathroom showers	2022-03-31	2022-04-13	Jeremy Reimer	10 days	40FS-3 days
42	18.0	Measure Shower Glass	2022-04-14	2022-04-14	Patsy	1 day?	41
43	18.0	Install Shower Glass	2022-04-27	2022-04-27	Patsy	1 day?	42FS+7 days
44	18.0	Fireplace Stone	2022-04-14	2022-04-20	Jeremy Reimer	4 days	41
45	21.0	Paint Primer Coat	2022-04-05	2022-04-13	Steve Nunn	7 days	40
46	17.0	Deliver Interior Doors & Trim	2022-04-11	2022-04-11	Patsy	1 day	47SS-3 days
47	17.0	Install Interior Doors & Trim	2022-04-14	2022-04-22	Joseph	6 days	45
48	21.0	Paint colour Coat	2022-04-25	2022-04-29	Steve Nunn	5 days	47
49	20.0	Deliver Ulay and Flooring	2022-04-25	2022-04-25	Patsy	1 day	47
50	20.0	Install Ulay	2022-04-26	2022-04-29	Joseph	4 days	49
51	20.0	Install Flooring	2022-04-26	2022-05-19	Rob	18 days	49
52	19.0	Install Cabinets and Vanities	2022-05-20	2022-05-31	Renaissance	7 days	51
53	19.0	Measure countertops	2022-06-01	2022-06-01	Colonial	1 day	52
54	19.0	Install Countertops	2022-06-16	2022-06-16	Colonial	1 day	53FS+10 day
55	17.0	Delivery Baseboards & Trim	2022-05-17	2022-05-17	Patsy	1 day	56SS-3 days
56	17.1	Install Baseboards & Trim	2022-05-20	2022-05-27	Joseph,Rob	5 days	51
57	21.0	Paint Baseboards & Trim	2022-05-30	2022-06-02	Steve Nunn	4 days	56
58	17.1	Final Fixtures	2022-05-30	2022-06-02	Joseph	4 days	56
59	17.0	Wire Closet Shelving	2022-06-03	2022-06-07	Gary Konrad	3 days	57
60	22.0	Order appliances	2022-04-13	2022-04-13	Patsy	1 day?	61FS-36 day
61	22.0	Appliance Delivery	2022-06-03	2022-06-03	Patsy	1 day	57
62	13.0	HVAC Appliance hookup	2022-06-06	2022-06-06	Ryan Burt	1 day	61
63	12.0	Plumbing Appliance hookup	2022-06-07	2022-06-07	JCL Plumbing	1 day	62
64	14.0	Electrical Appliance hookup	2022-06-08	2022-06-08	All Phase Electric	1 day	63
65	13.0	Fireplace Activation	2022-06-03	2022-06-03	SA Fireplace	1 day	57
66	1.7	Conditional Occupancy Inspection	2022-06-09	2022-06-09	Sicamous,Marc	1 day?	64
67	20.0	Install carpet on stairs	2022-06-10	2022-06-10	Nufloors	1 day	66
68	9.0	Install overhead doors garage	2022-06-10	2022-06-10	Vision Overhead doors	1 day?	66
69	21.0	Final Paint	2022-06-13	2022-06-13	Steve Nunn	1 day?	67
70	17.0	Clean home	2022-06-14	2022-06-15	TBD	2 days	69
71	17.0	Customer Occupancy Walkthrough	2022-06-16	2022-06-16	Allison,Mike Adkins	1 day?	70
72	17.0	Resolve Deficiencies	2022-06-17	2022-06-23	Joseph	5 days	71
73	1.0	Occupancy Date	2022-06-24	2022-06-24	Allison,Mike Adkins	1 day	72
